

ID	Task Name	Duration	Start	Finish	March	May	July	September	November	January	March	May	July	September
1	Digital Council Programme 16/17	426 days	Thu 10/03/16	Thu 26/10/17										
2	Digital Council PgM Board	261 days	Fri 01/04/16	Fri 31/03/17										
3	Board	1.5 hrs	Mon 18/04/16	Mon 18/04/16										
4	Board	1.5 hrs	Mon 23/05/16	Mon 23/05/16										
5	Board	1.5 hrs	Mon 20/06/16	Mon 20/06/16										
6	Board	1.5 hrs	Mon 18/07/16	Mon 18/07/16										
7	Board	1.5 hrs	Mon 15/08/16	Mon 15/08/16										
8	Board	1.5 hrs	Wed 21/09/16	Wed 21/09/16										
9	Board	1.5 hrs	Mon 17/10/16	Mon 17/10/16										
10	Board	1.5 hrs	Mon 21/11/16	Mon 21/11/16										
11	Board	1.5 hrs	Mon 19/12/16	Mon 19/12/16										
12	Board	1.5 hrs	Mon 16/01/17	Mon 16/01/17										
13	Board	1.5 hrs	Mon 20/02/17	Mon 20/02/17										
14	Board	1.5 hrs	Mon 20/03/17	Mon 20/03/17										
15	Digital Council - CS Target	261 days	Fri 01/04/16	Fri 31/03/17										
16	Q1 25%	65 days	Fri 01/04/16	Thu 30/06/16										
17	Q2 32%	66 days	Fri 01/07/16	Fri 30/09/16										
18	Q3 42%	66 days	Mon 03/10/16	Sat 31/12/16										
19	Q4 - 55%	65 days	Mon 02/01/17	Fri 31/03/17										
20	Digital Council Efficiency Target	261 days	Fri 01/04/16	Fri 31/03/17										
21	Q1 £3.02m	65 days	Fri 01/04/16	Thu 30/06/16										
22	Q2 £3.65m	66 days	Fri 01/07/16	Fri 30/09/16										
23	Q3 £4.27m	65 days	Mon 03/10/16	Fri 30/12/16										


Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	March	May	July	September	November	January	March	May	July	September
24	Q4 £5.00m	65 days	Mon 02/01/17	Fri 31/03/17										
25	Digital Council Sprint	279 days	Fri 01/04/16	Wed 26/04/17	[Timeline bar from March to September]									
26	Sprint 14	17 days	Fri 01/04/16	Mon 25/04/16	[Task bar]									
27	Sprint 15	18 days	Tue 26/04/16	Thu 19/05/16		[Task bar]								
28	Sprint 16	14 days	Fri 20/05/16	Wed 08/06/16			[Task bar]							
29	Sprint 17	15 days	Thu 09/06/16	Wed 29/06/16				[Task bar]						
30	Sprint 18	15 days	Thu 30/06/16	Wed 20/07/16					[Task bar]					
31	Sprint 19	15 days	Thu 21/07/16	Wed 10/08/16						[Task bar]				
32	Sprint 20	15 days	Thu 11/08/16	Wed 31/08/16							[Task bar]			
33	Sprint 21	15 days	Thu 01/09/16	Wed 21/09/16								[Task bar]		
34	Sprint 22	15 days	Thu 22/09/16	Wed 12/10/16									[Task bar]	
35	Sprint 23	15 days	Thu 13/10/16	Wed 02/11/16										[Task bar]
36	Sprint 24	15 days	Thu 03/11/16	Wed 23/11/16										[Task bar]
37	Sprint 25	15 days	Thu 24/11/16	Wed 14/12/16										[Task bar]
38	Sprint 26	20 days	Thu 15/12/16	Wed 11/01/17										[Task bar]
39	Sprint 27	15 days	Thu 12/01/17	Wed 01/02/17										[Task bar]
40	Sprint 28	15 days	Thu 02/02/17	Wed 22/02/17										[Task bar]
41	Sprint 29	15 days	Thu 23/02/17	Wed 15/03/17										[Task bar]
42	Sprint 30	15 days	Thu 16/03/17	Wed 05/04/17										[Task bar]
43	Sprint 31	15 days	Thu 06/04/17	Wed 26/04/17										[Task bar]
44	Learning & Opportunities & Children's Trust	376 days	Thu 19/05/16	Thu 26/10/17	[Timeline bar from May to October]									
45	Engage	14 days	Thu 19/05/16	Tue 07/06/16		[Task bar]								
46	Define	14 days	Wed 08/06/16	Mon 27/06/16			[Task bar]							


Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			




Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

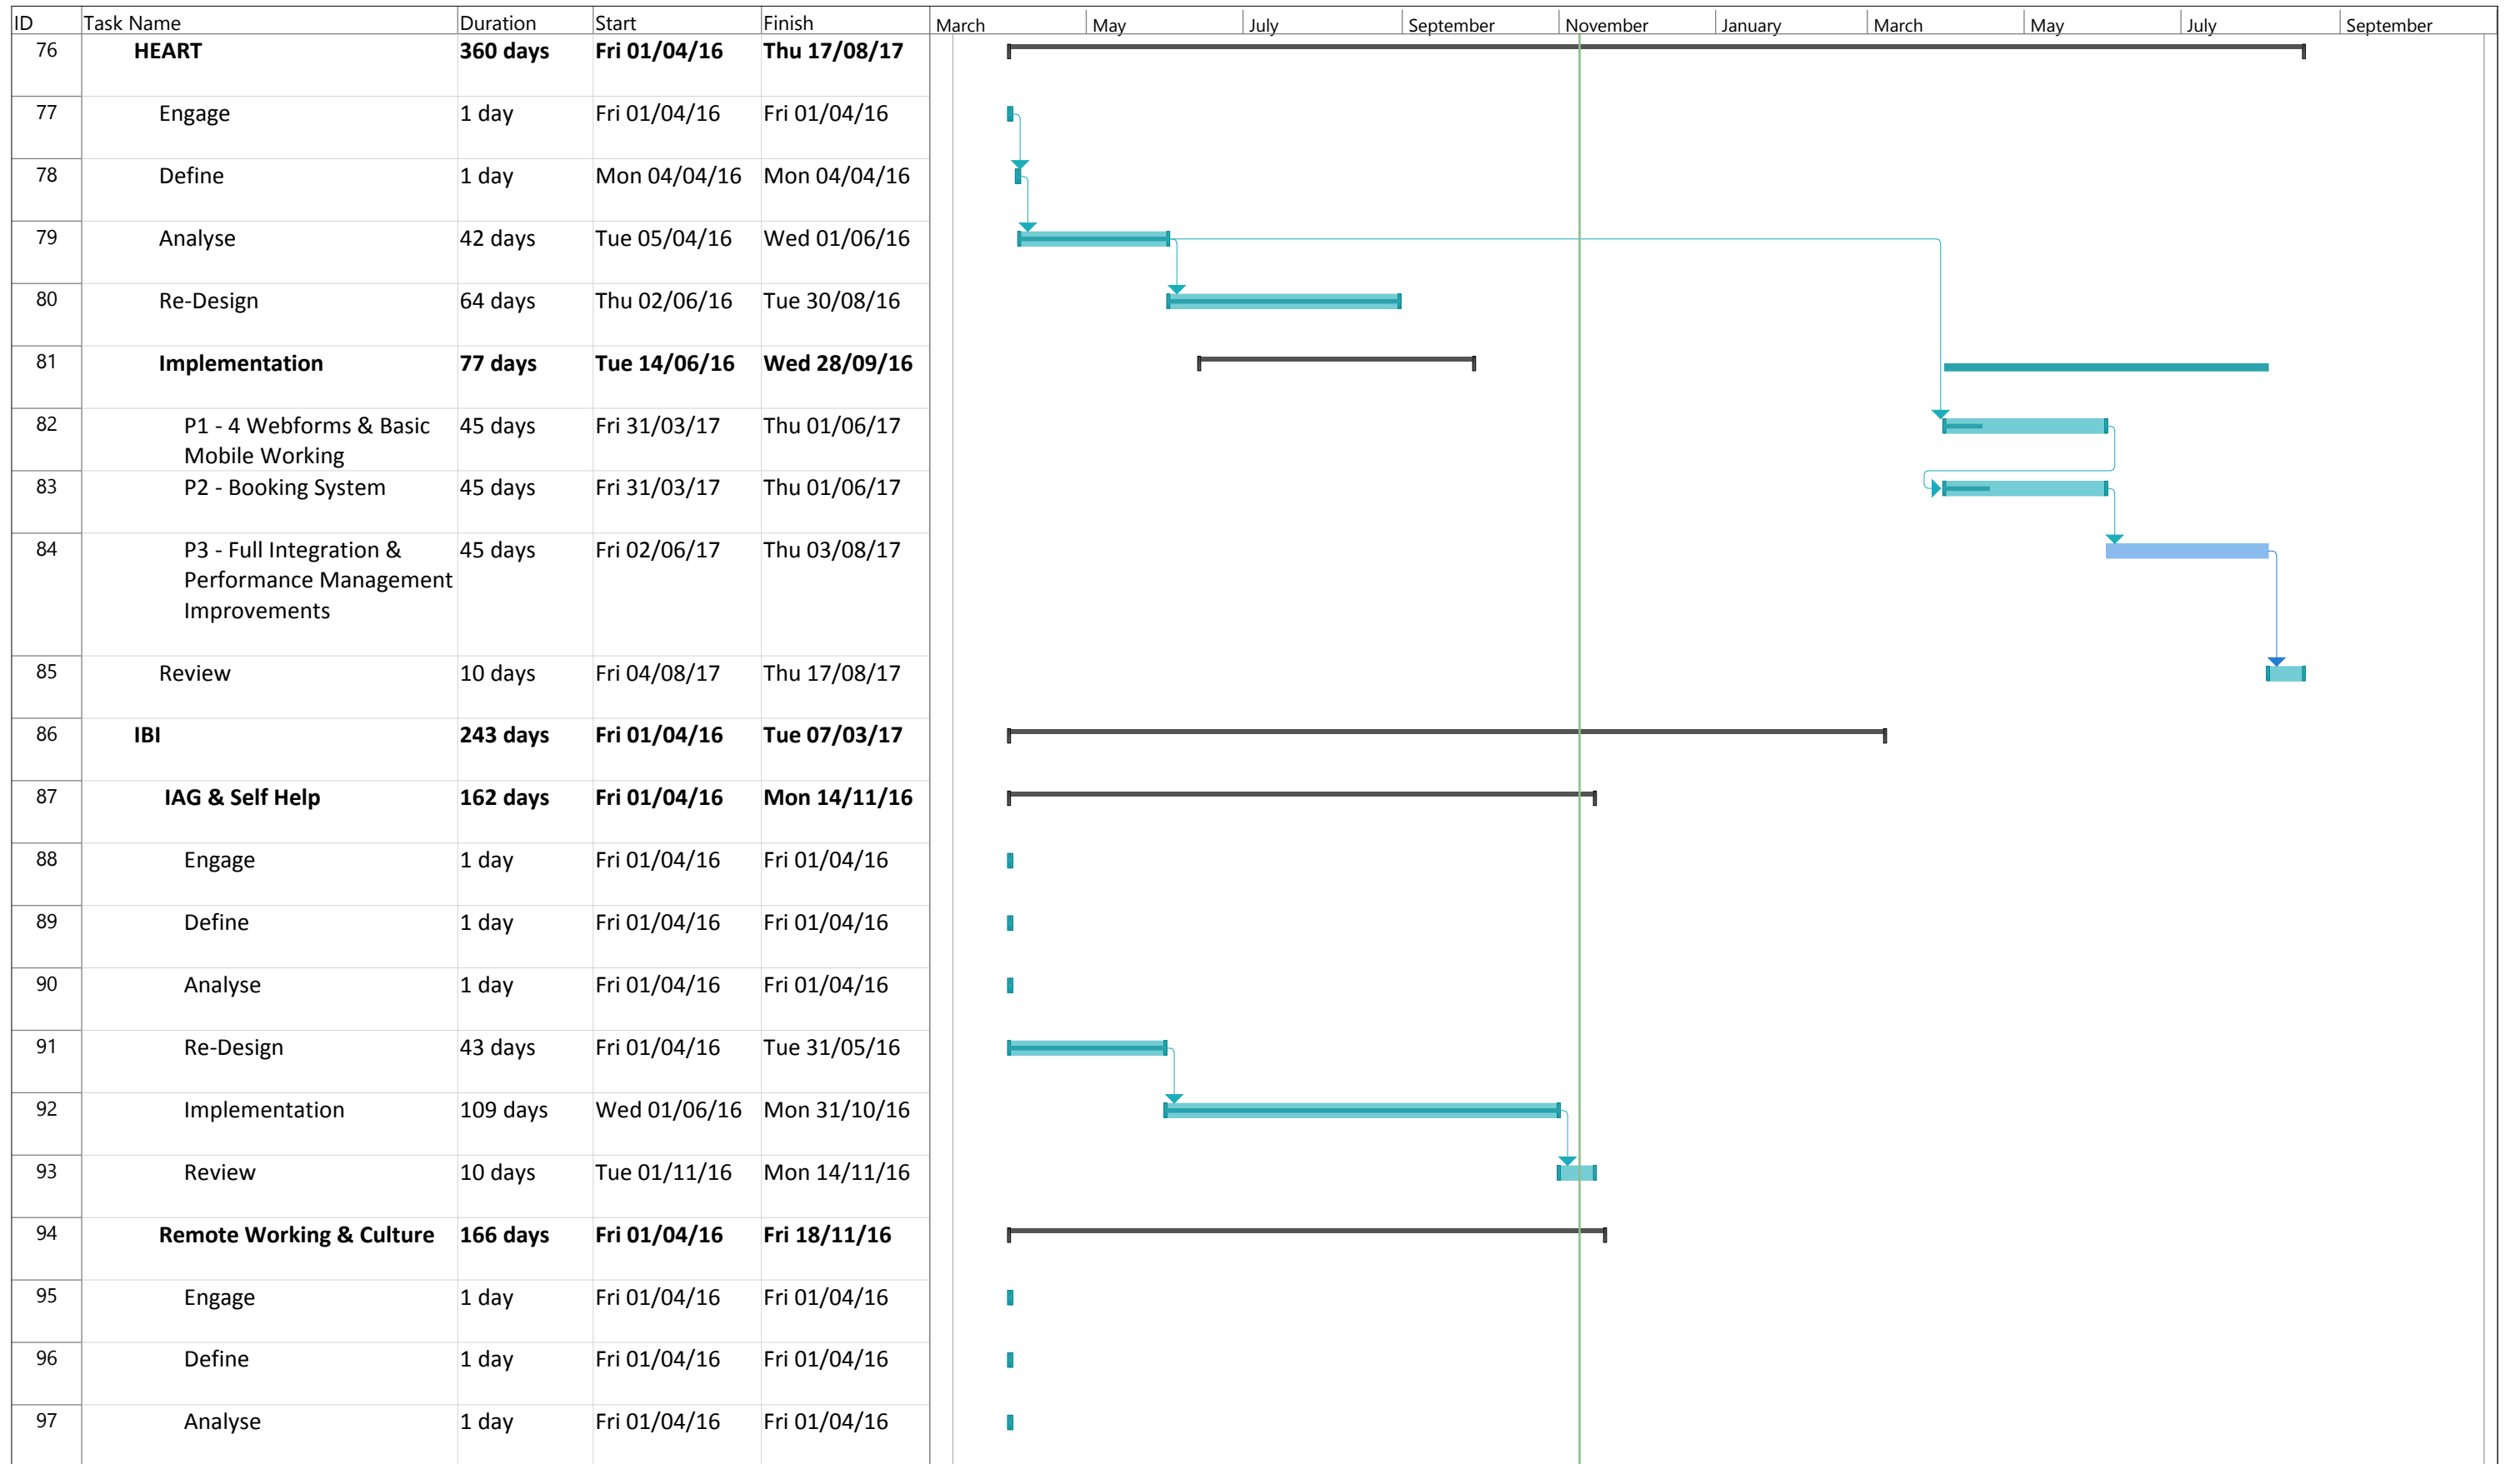


Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

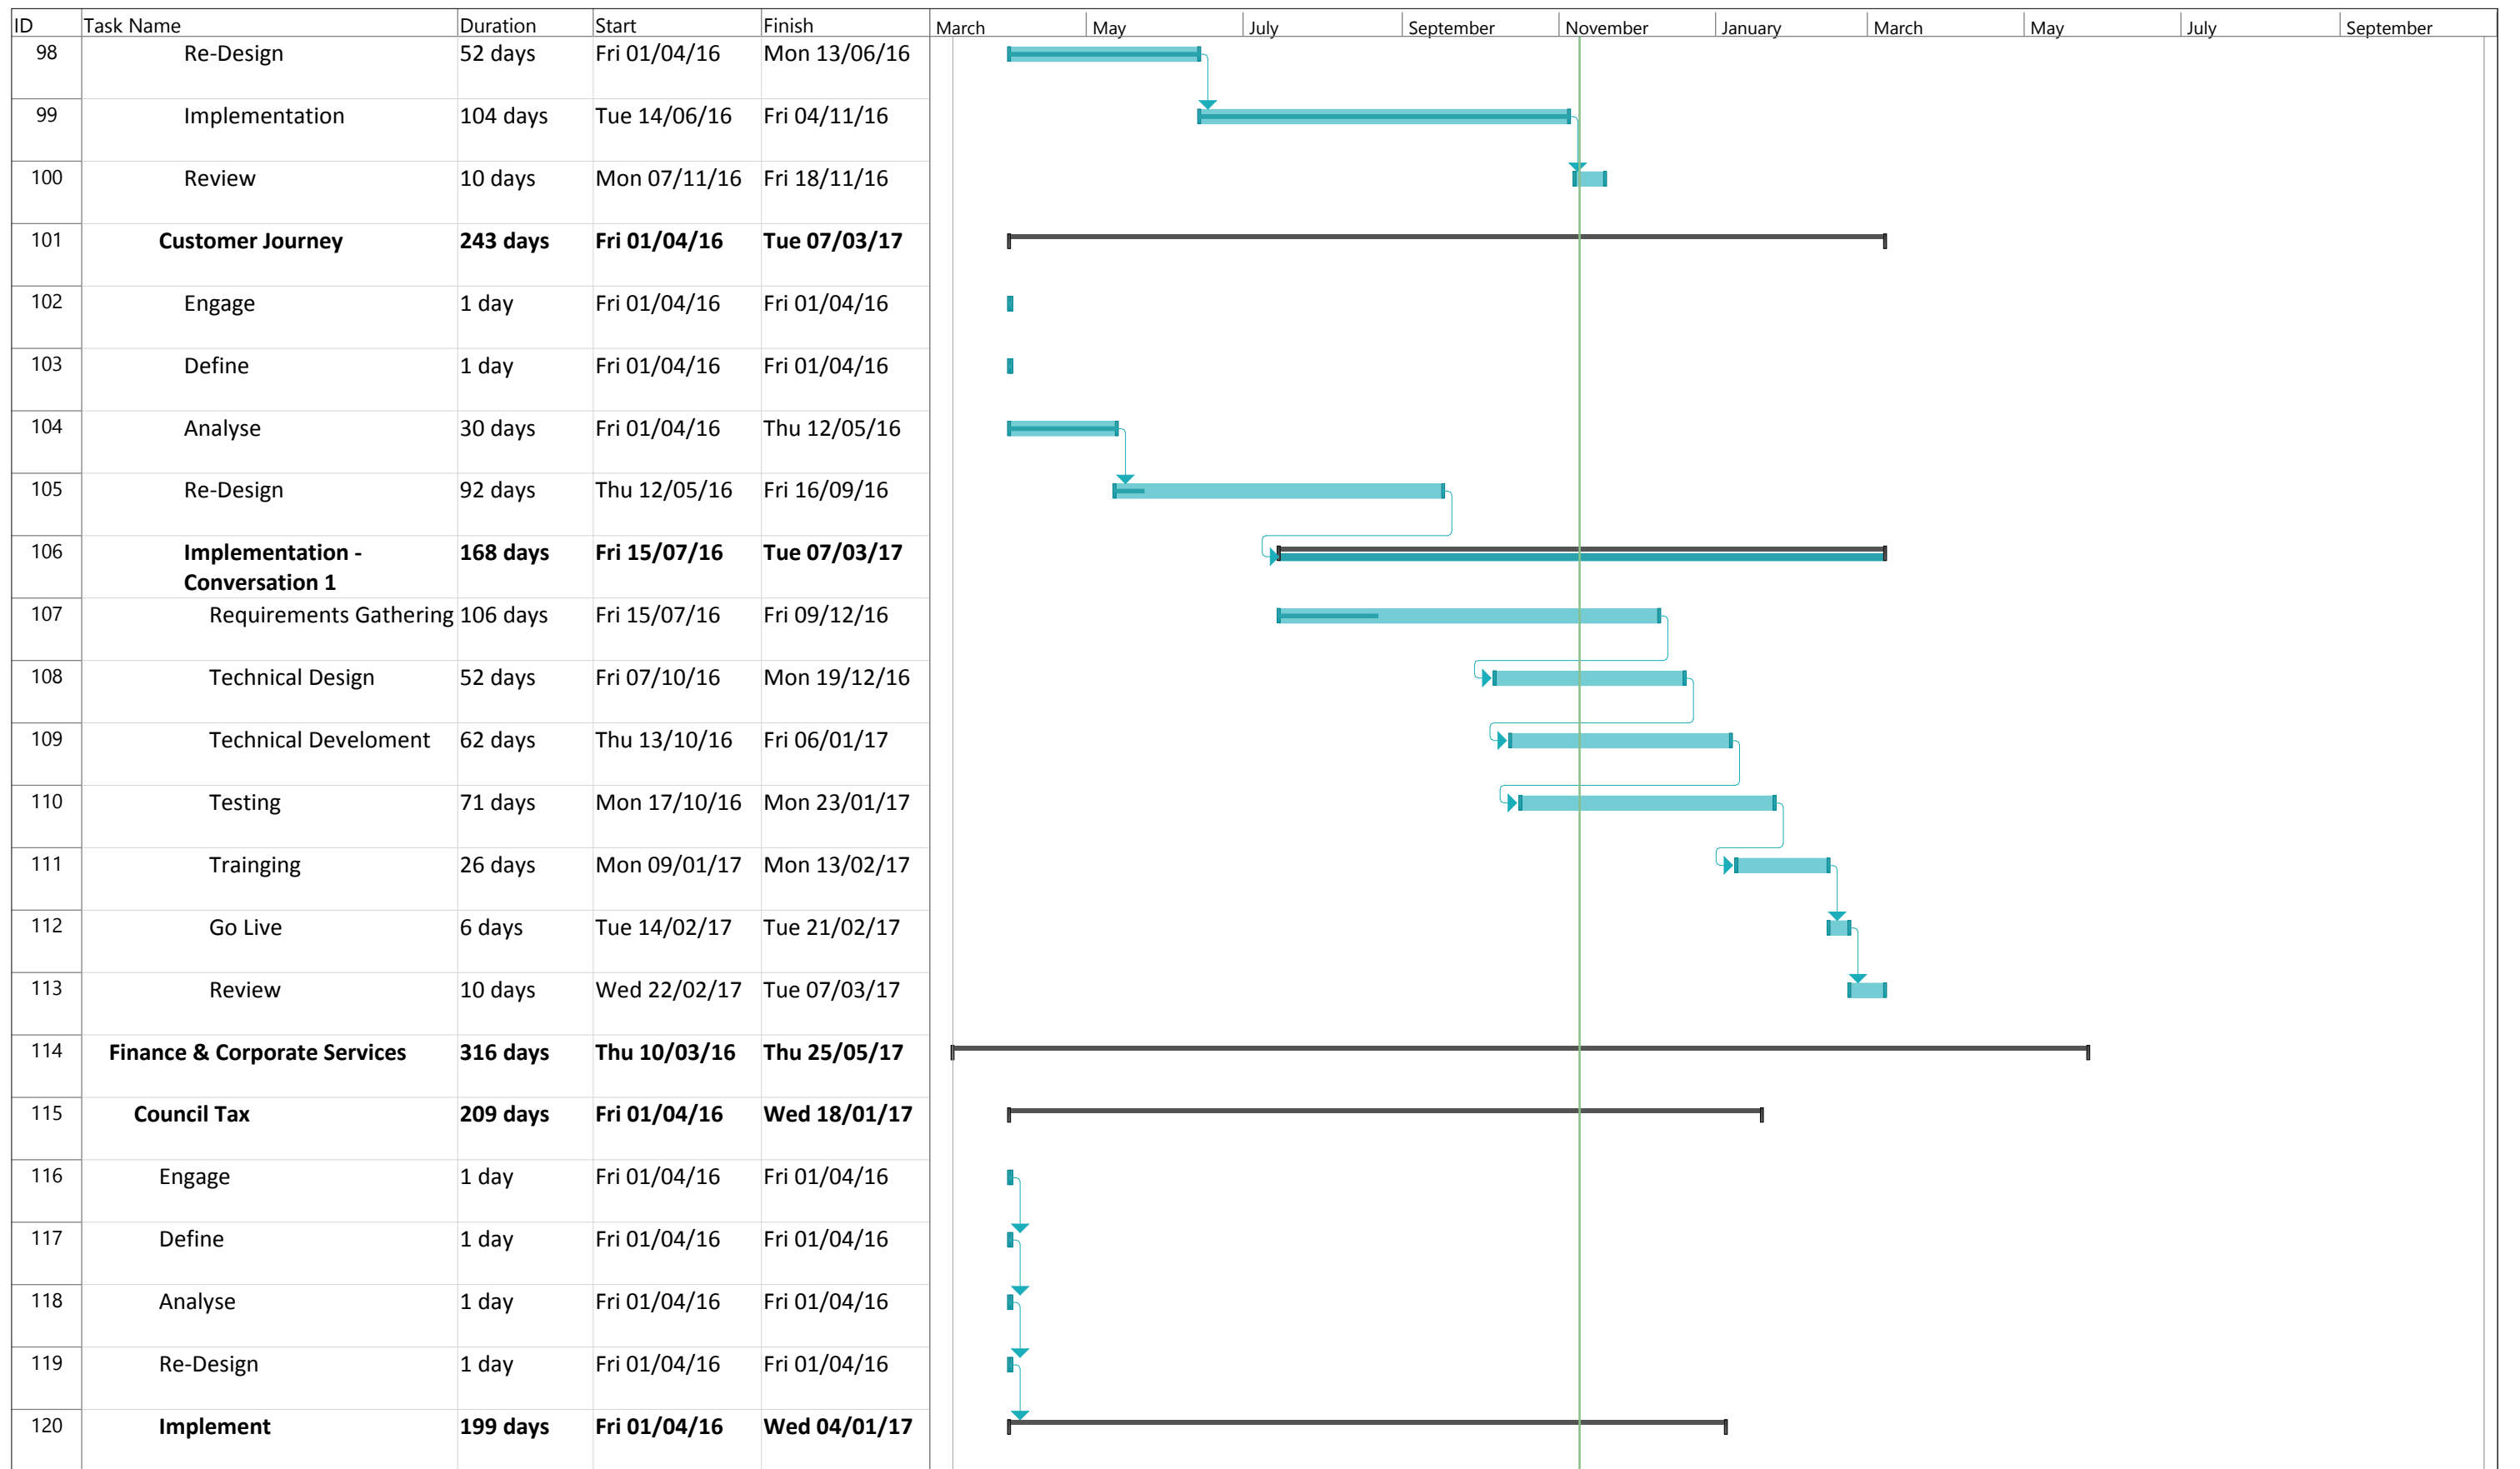


Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

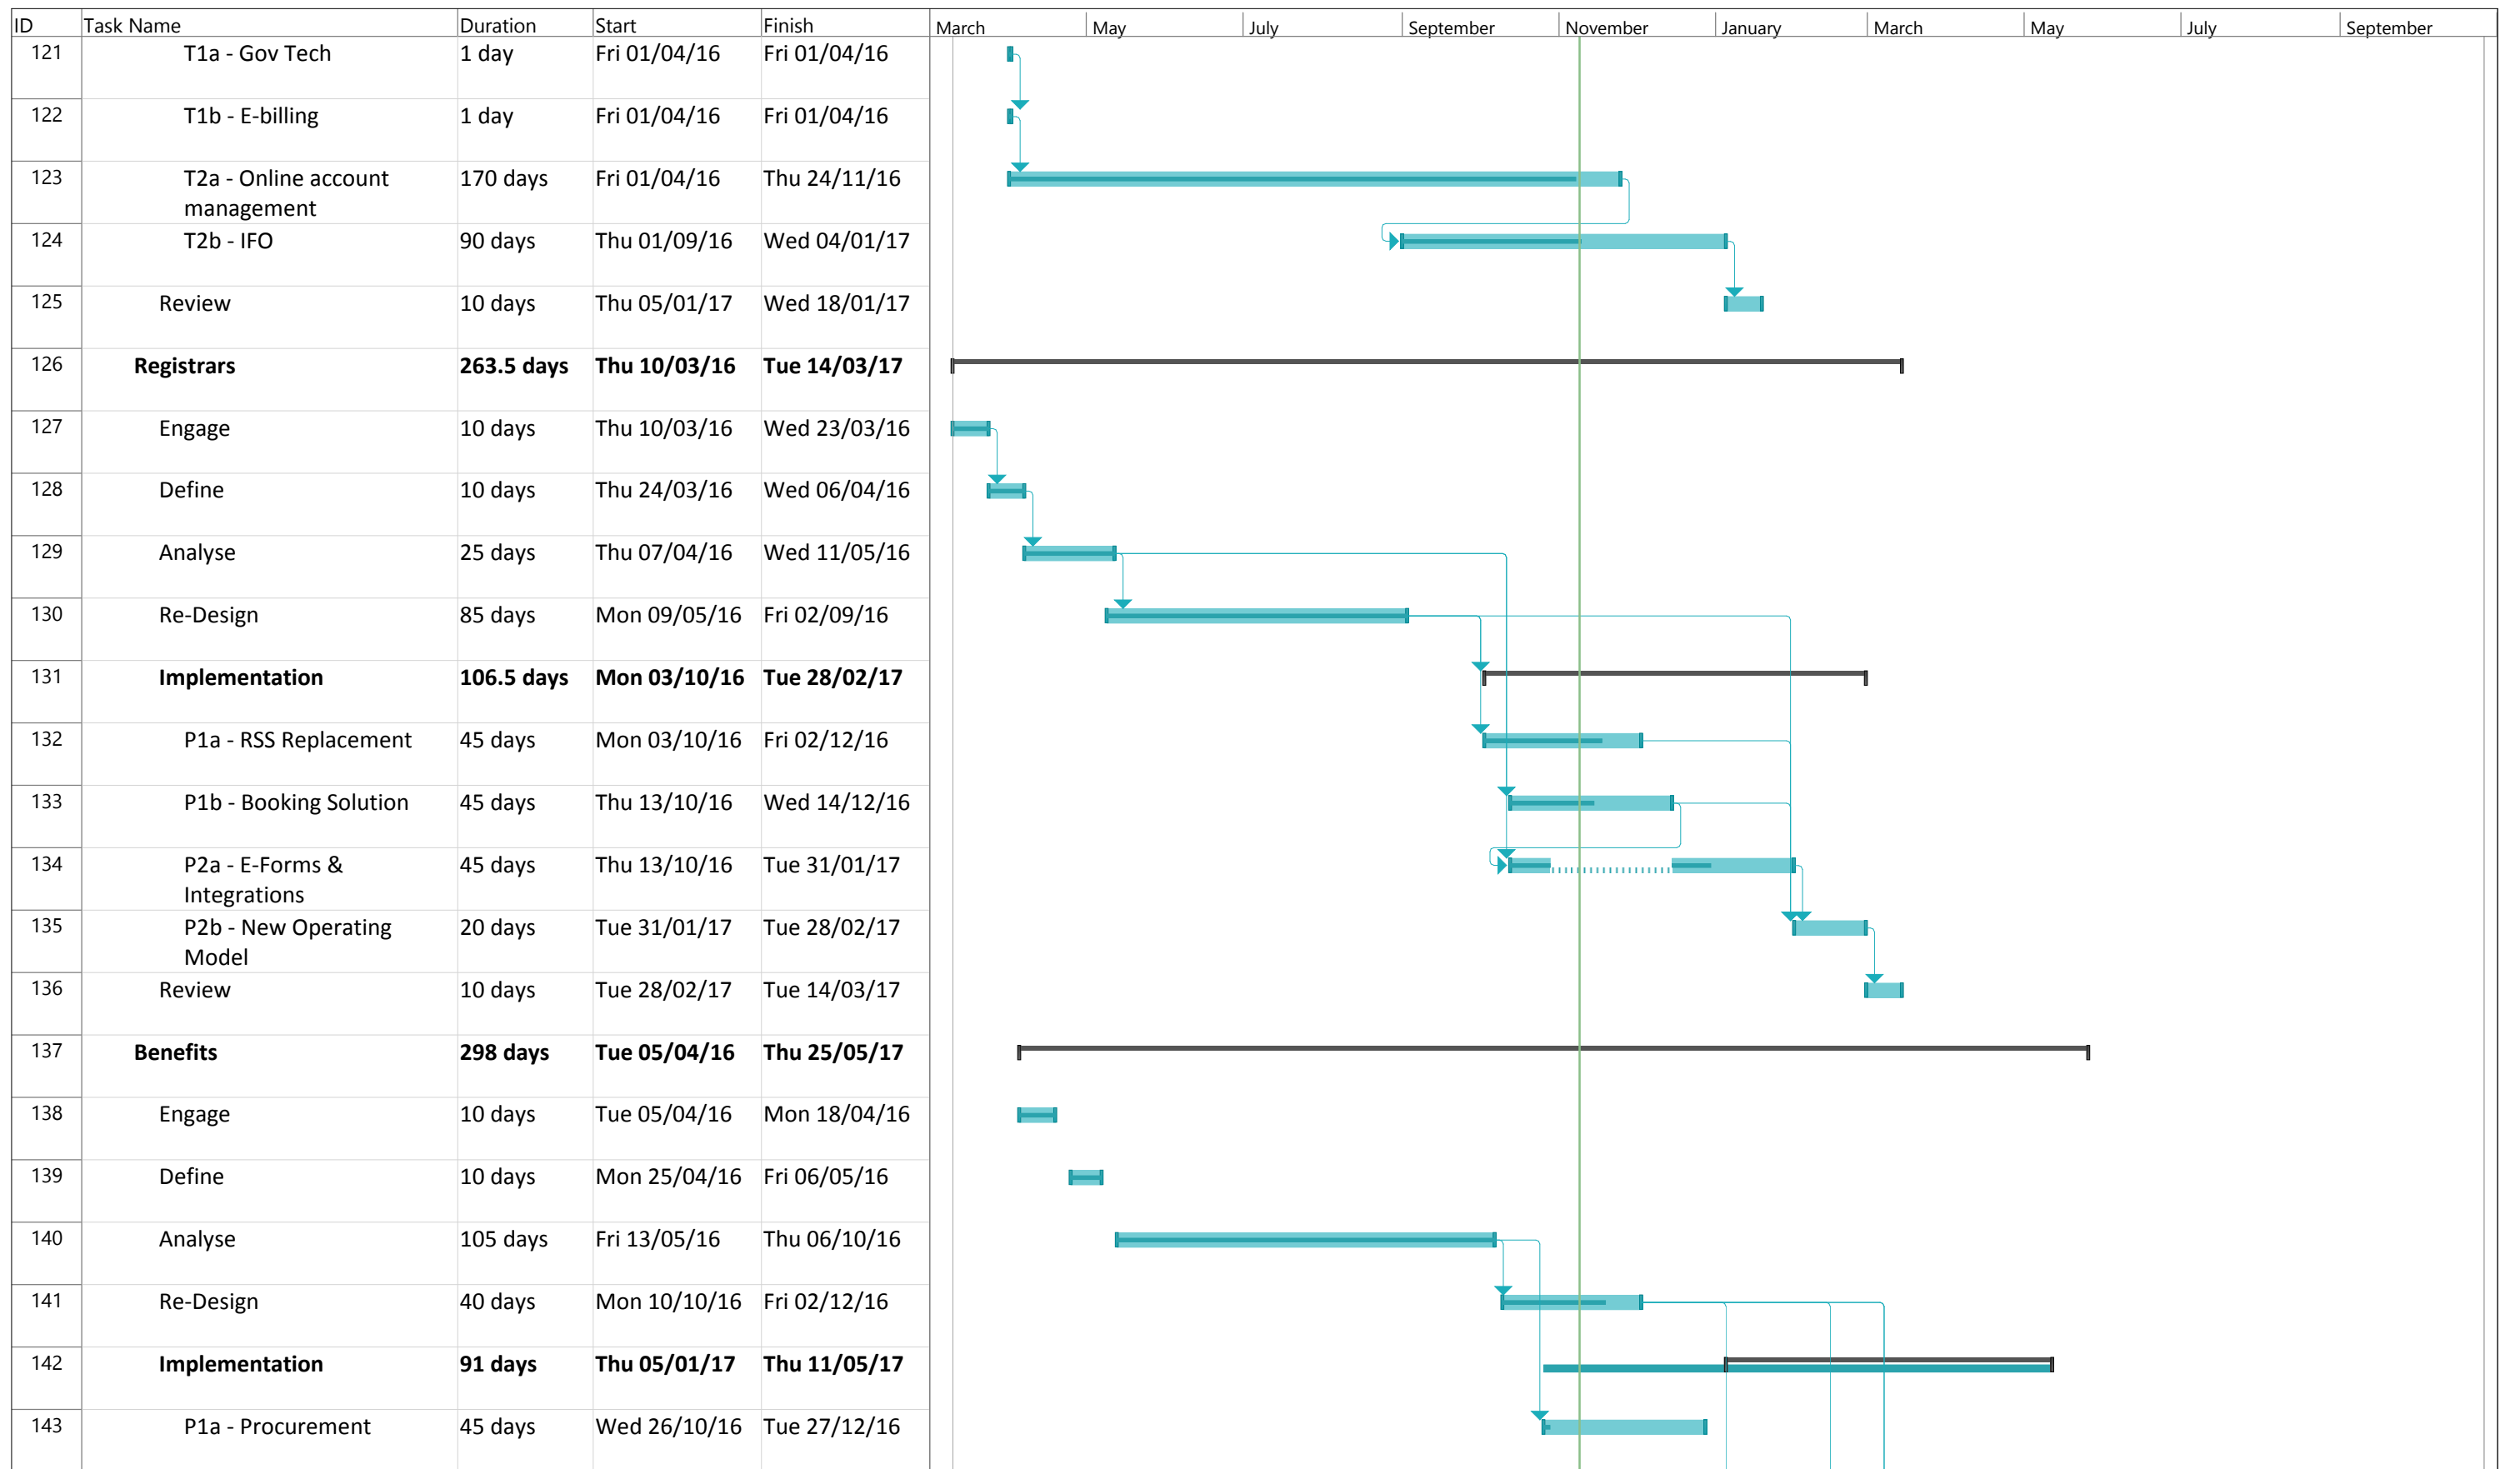


Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

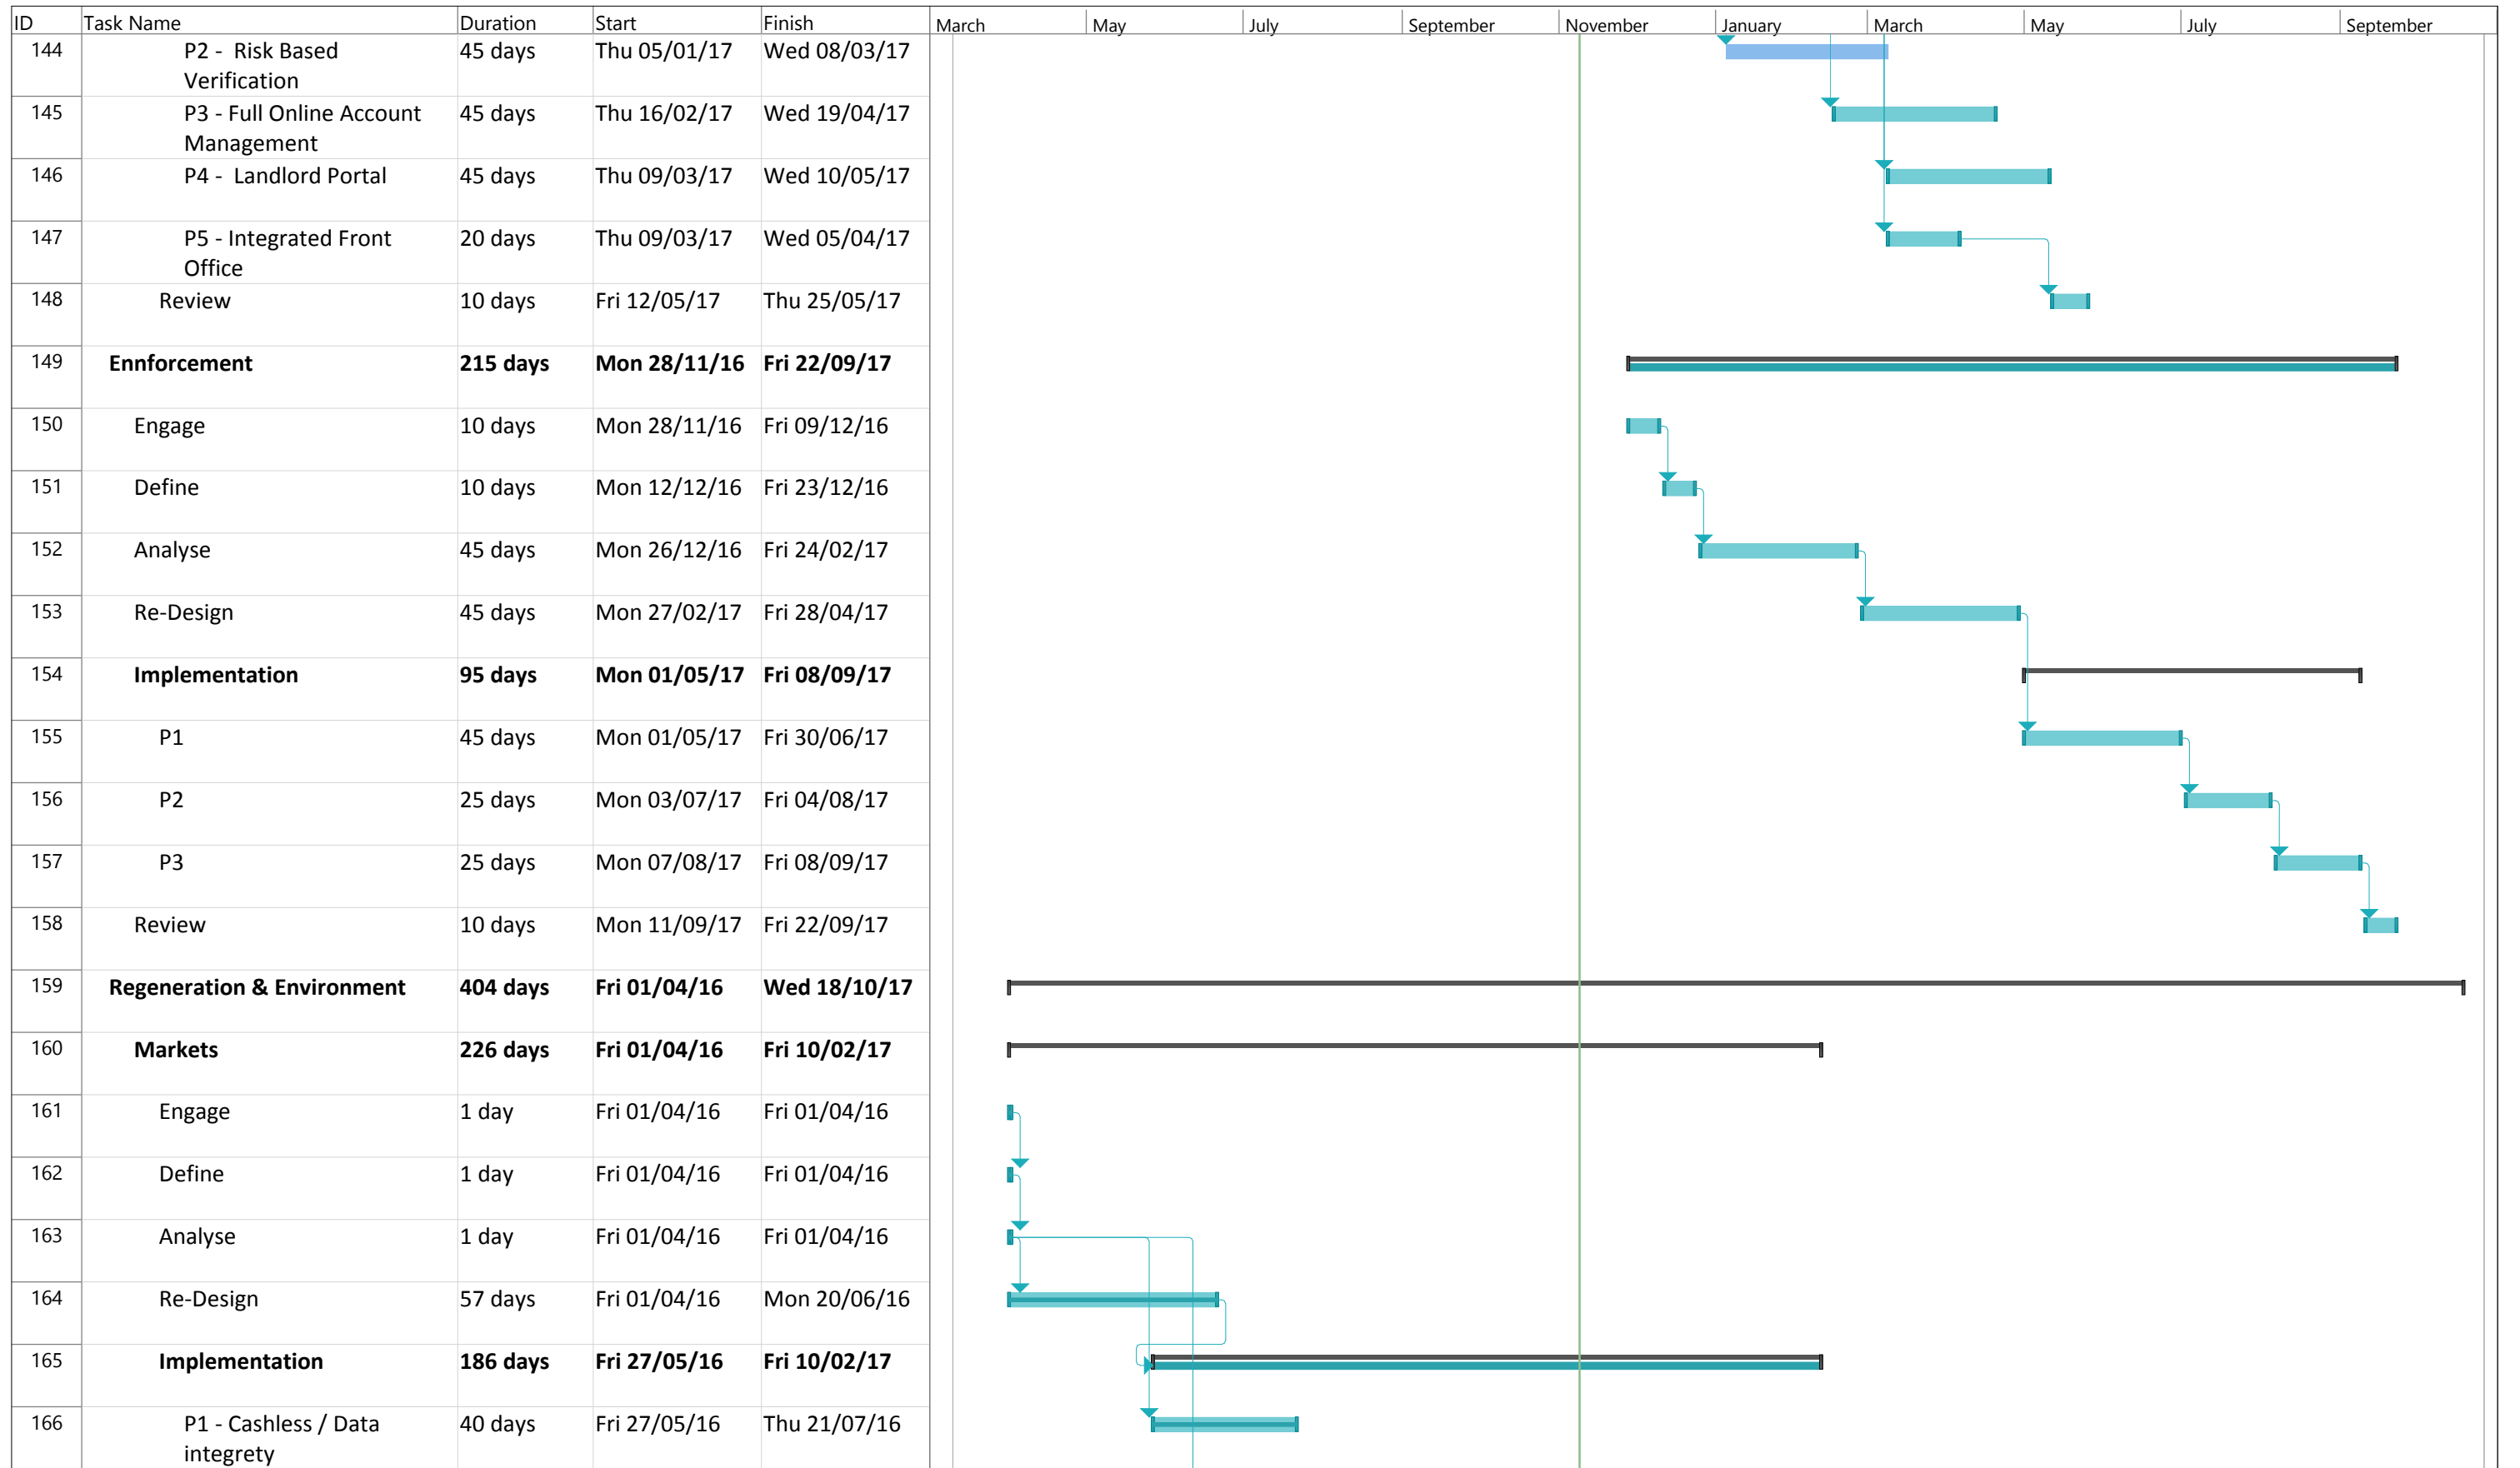

Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

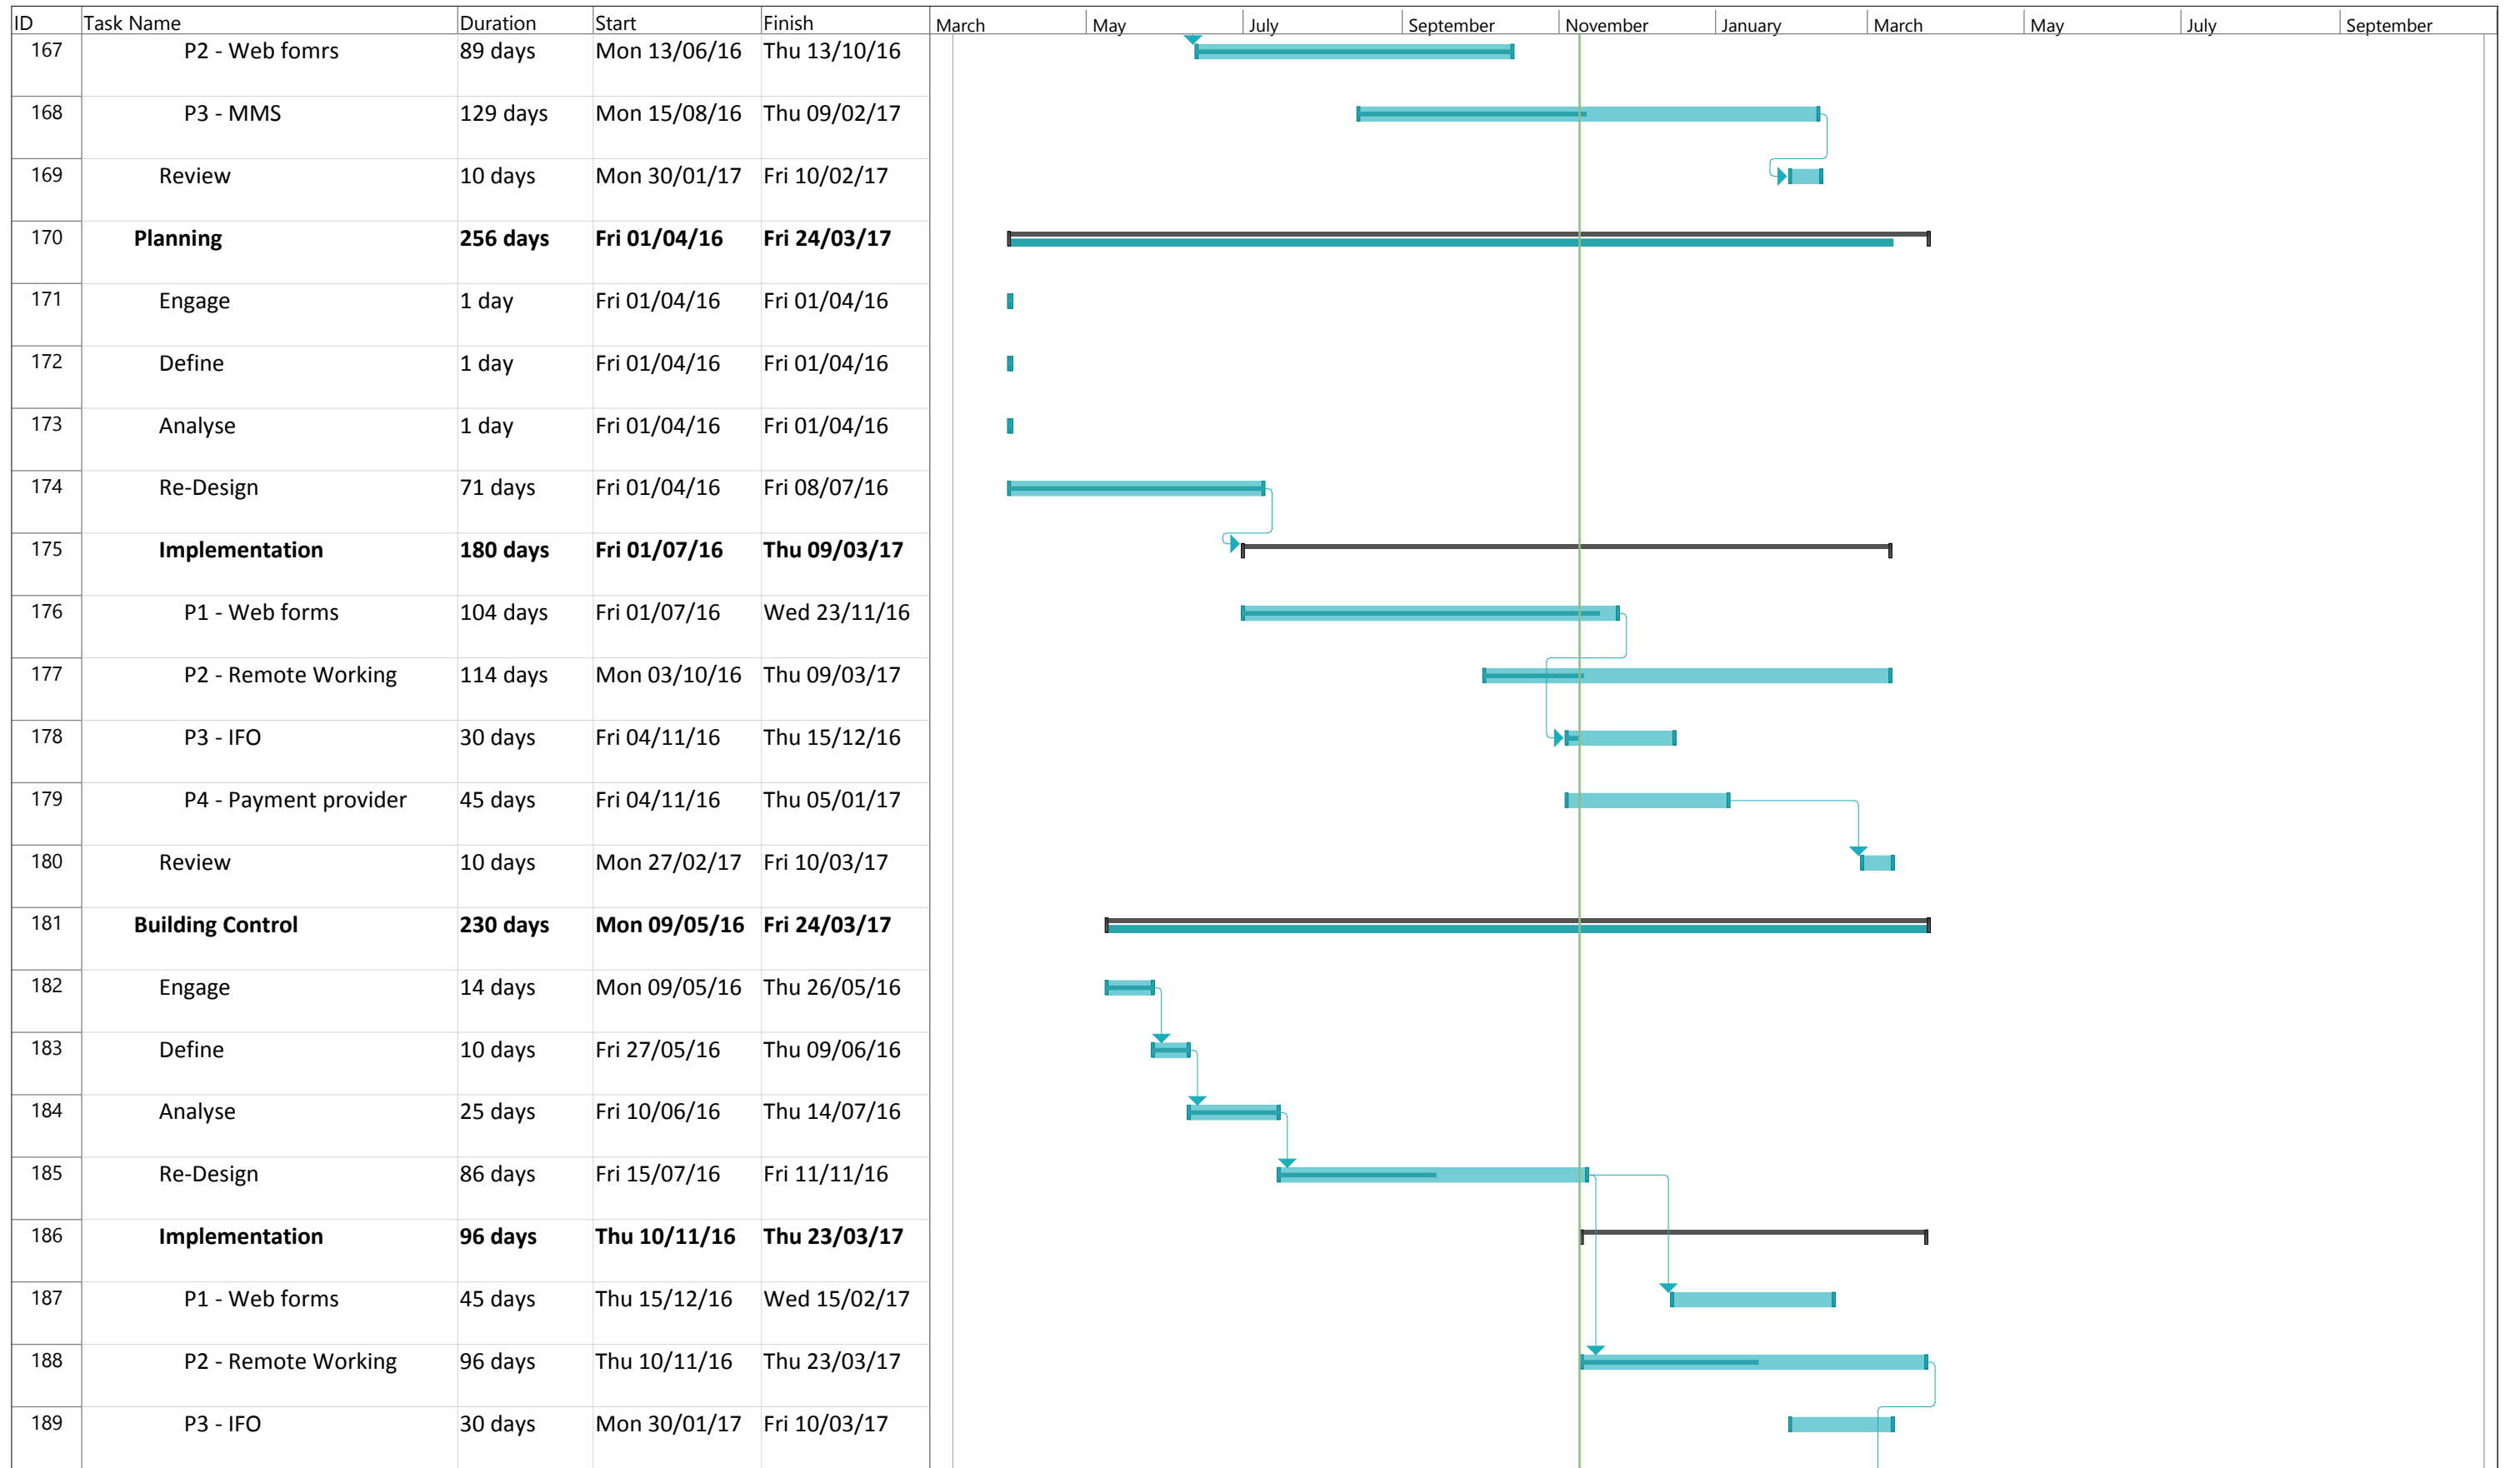


Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

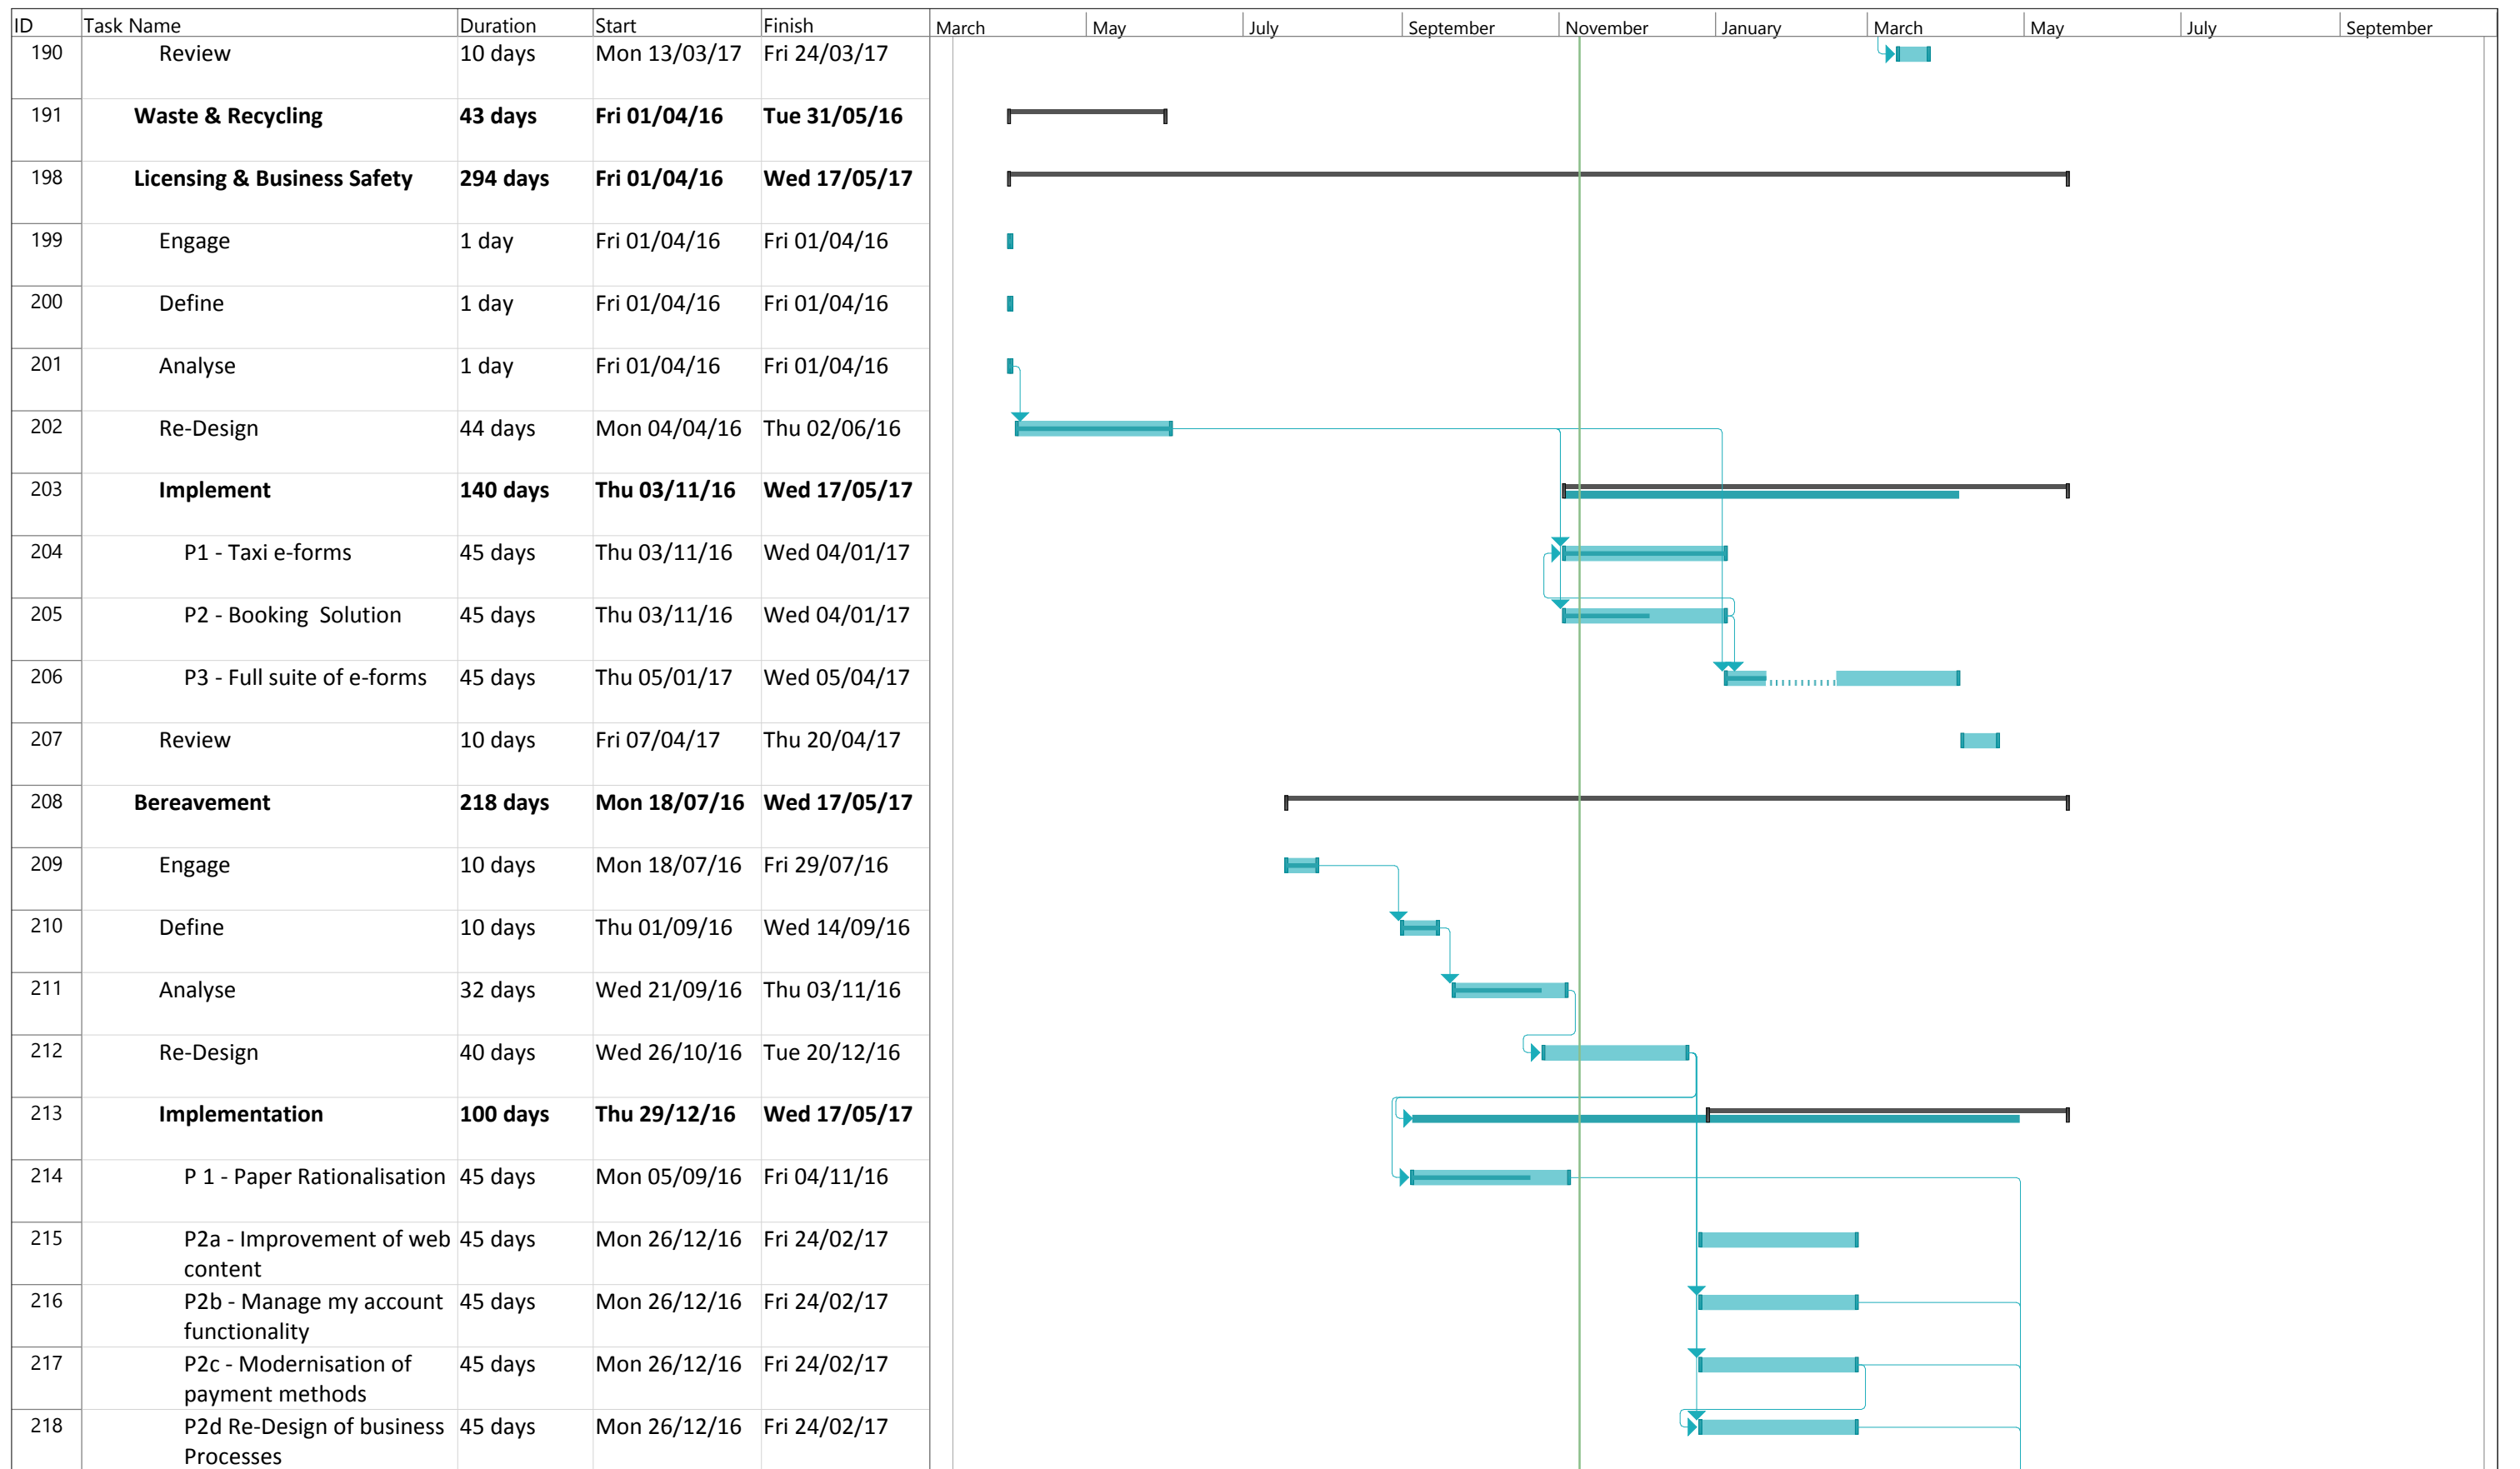

Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	March	May	July	September	November	January	March	May	July	September
219	P3 New Customer contact model	45 days	Mon 27/02/17	Fri 28/04/17										
220	P4 - Outsourcing of in house functions	45 days	Mon 27/02/17	Fri 28/04/17										
221	P5 Expansion of Rose Hill to offer new services and boost revenue	45 days	Mon 27/02/17	Fri 28/04/17										
222	Review	10 days	Mon 01/05/17	Fri 12/05/17										
223	Zero Fares	120 days	Fri 01/04/16	Thu 15/09/16										
232	Transport	230 days	Thu 01/12/16	Wed 18/10/17										
233	Engage	10 days	Thu 01/12/16	Wed 14/12/16										
234	Define	10 days	Thu 15/12/16	Wed 28/12/16										
235	Analyse	25 days	Thu 29/12/16	Wed 01/02/17										
236	Re-Design	40 days	Thu 02/02/17	Wed 29/03/17										
237	Implement	145 days	Thu 30/03/17	Wed 18/10/17										
238	P1 - TBD	45 days	Thu 30/03/17	Wed 31/05/17										
239	P2 - TBD	45 days	Thu 01/06/17	Wed 02/08/17										
240	P3 - TBD	45 days	Thu 03/08/17	Wed 04/10/17										
241	Review	10 days	Thu 05/10/17	Wed 18/10/17										
242	Strategic Housing	114 days	Fri 01/04/16	Wed 07/09/16										
249	Cross Cutting	378 days	Fri 01/04/16	Tue 12/09/17										
250	Internal Services	288 days	Mon 06/06/16	Wed 12/07/17										
251	Finance & Corporate Services	261 days	Mon 06/06/16	Mon 05/06/17										
252	Engage	10 days	Mon 20/06/16	Fri 01/07/16										
253	Define	10 days	Fri 29/07/16	Thu 11/08/16										
254	Analyse	25 days	Mon 12/09/16	Fri 14/10/16										

Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

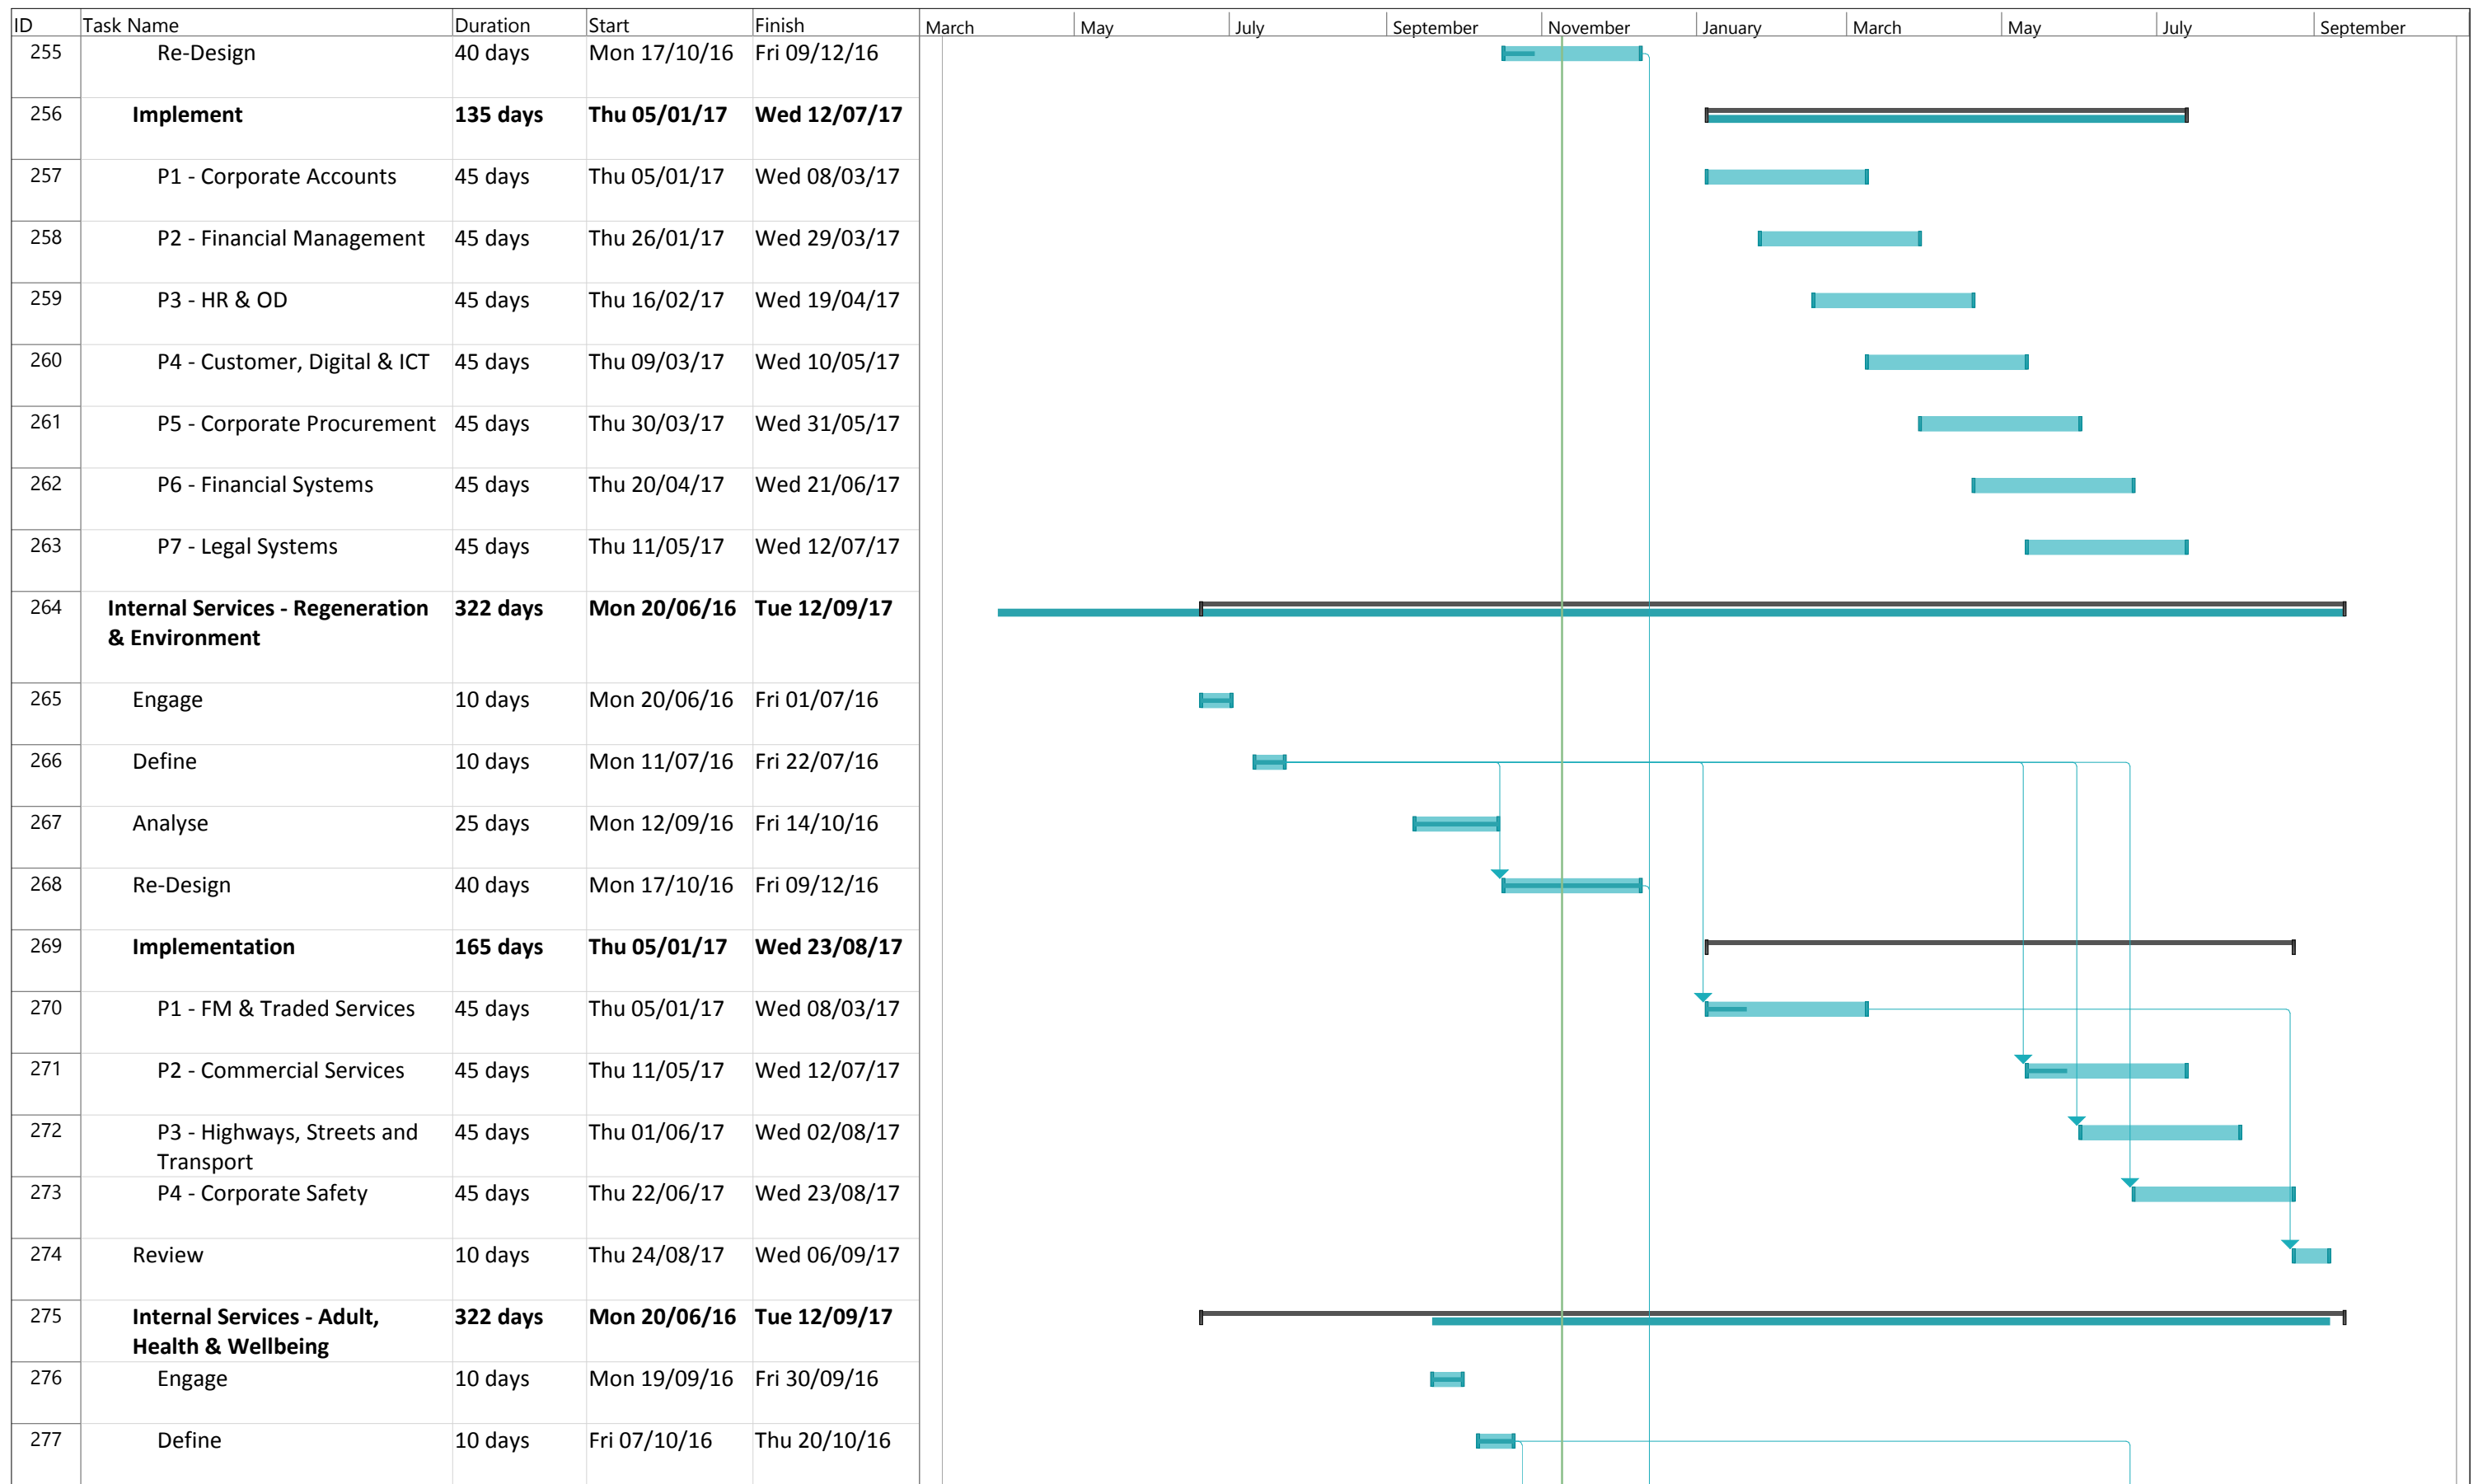


Project: Programme Plan - Sprin
Date: Wed 09/11/16

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

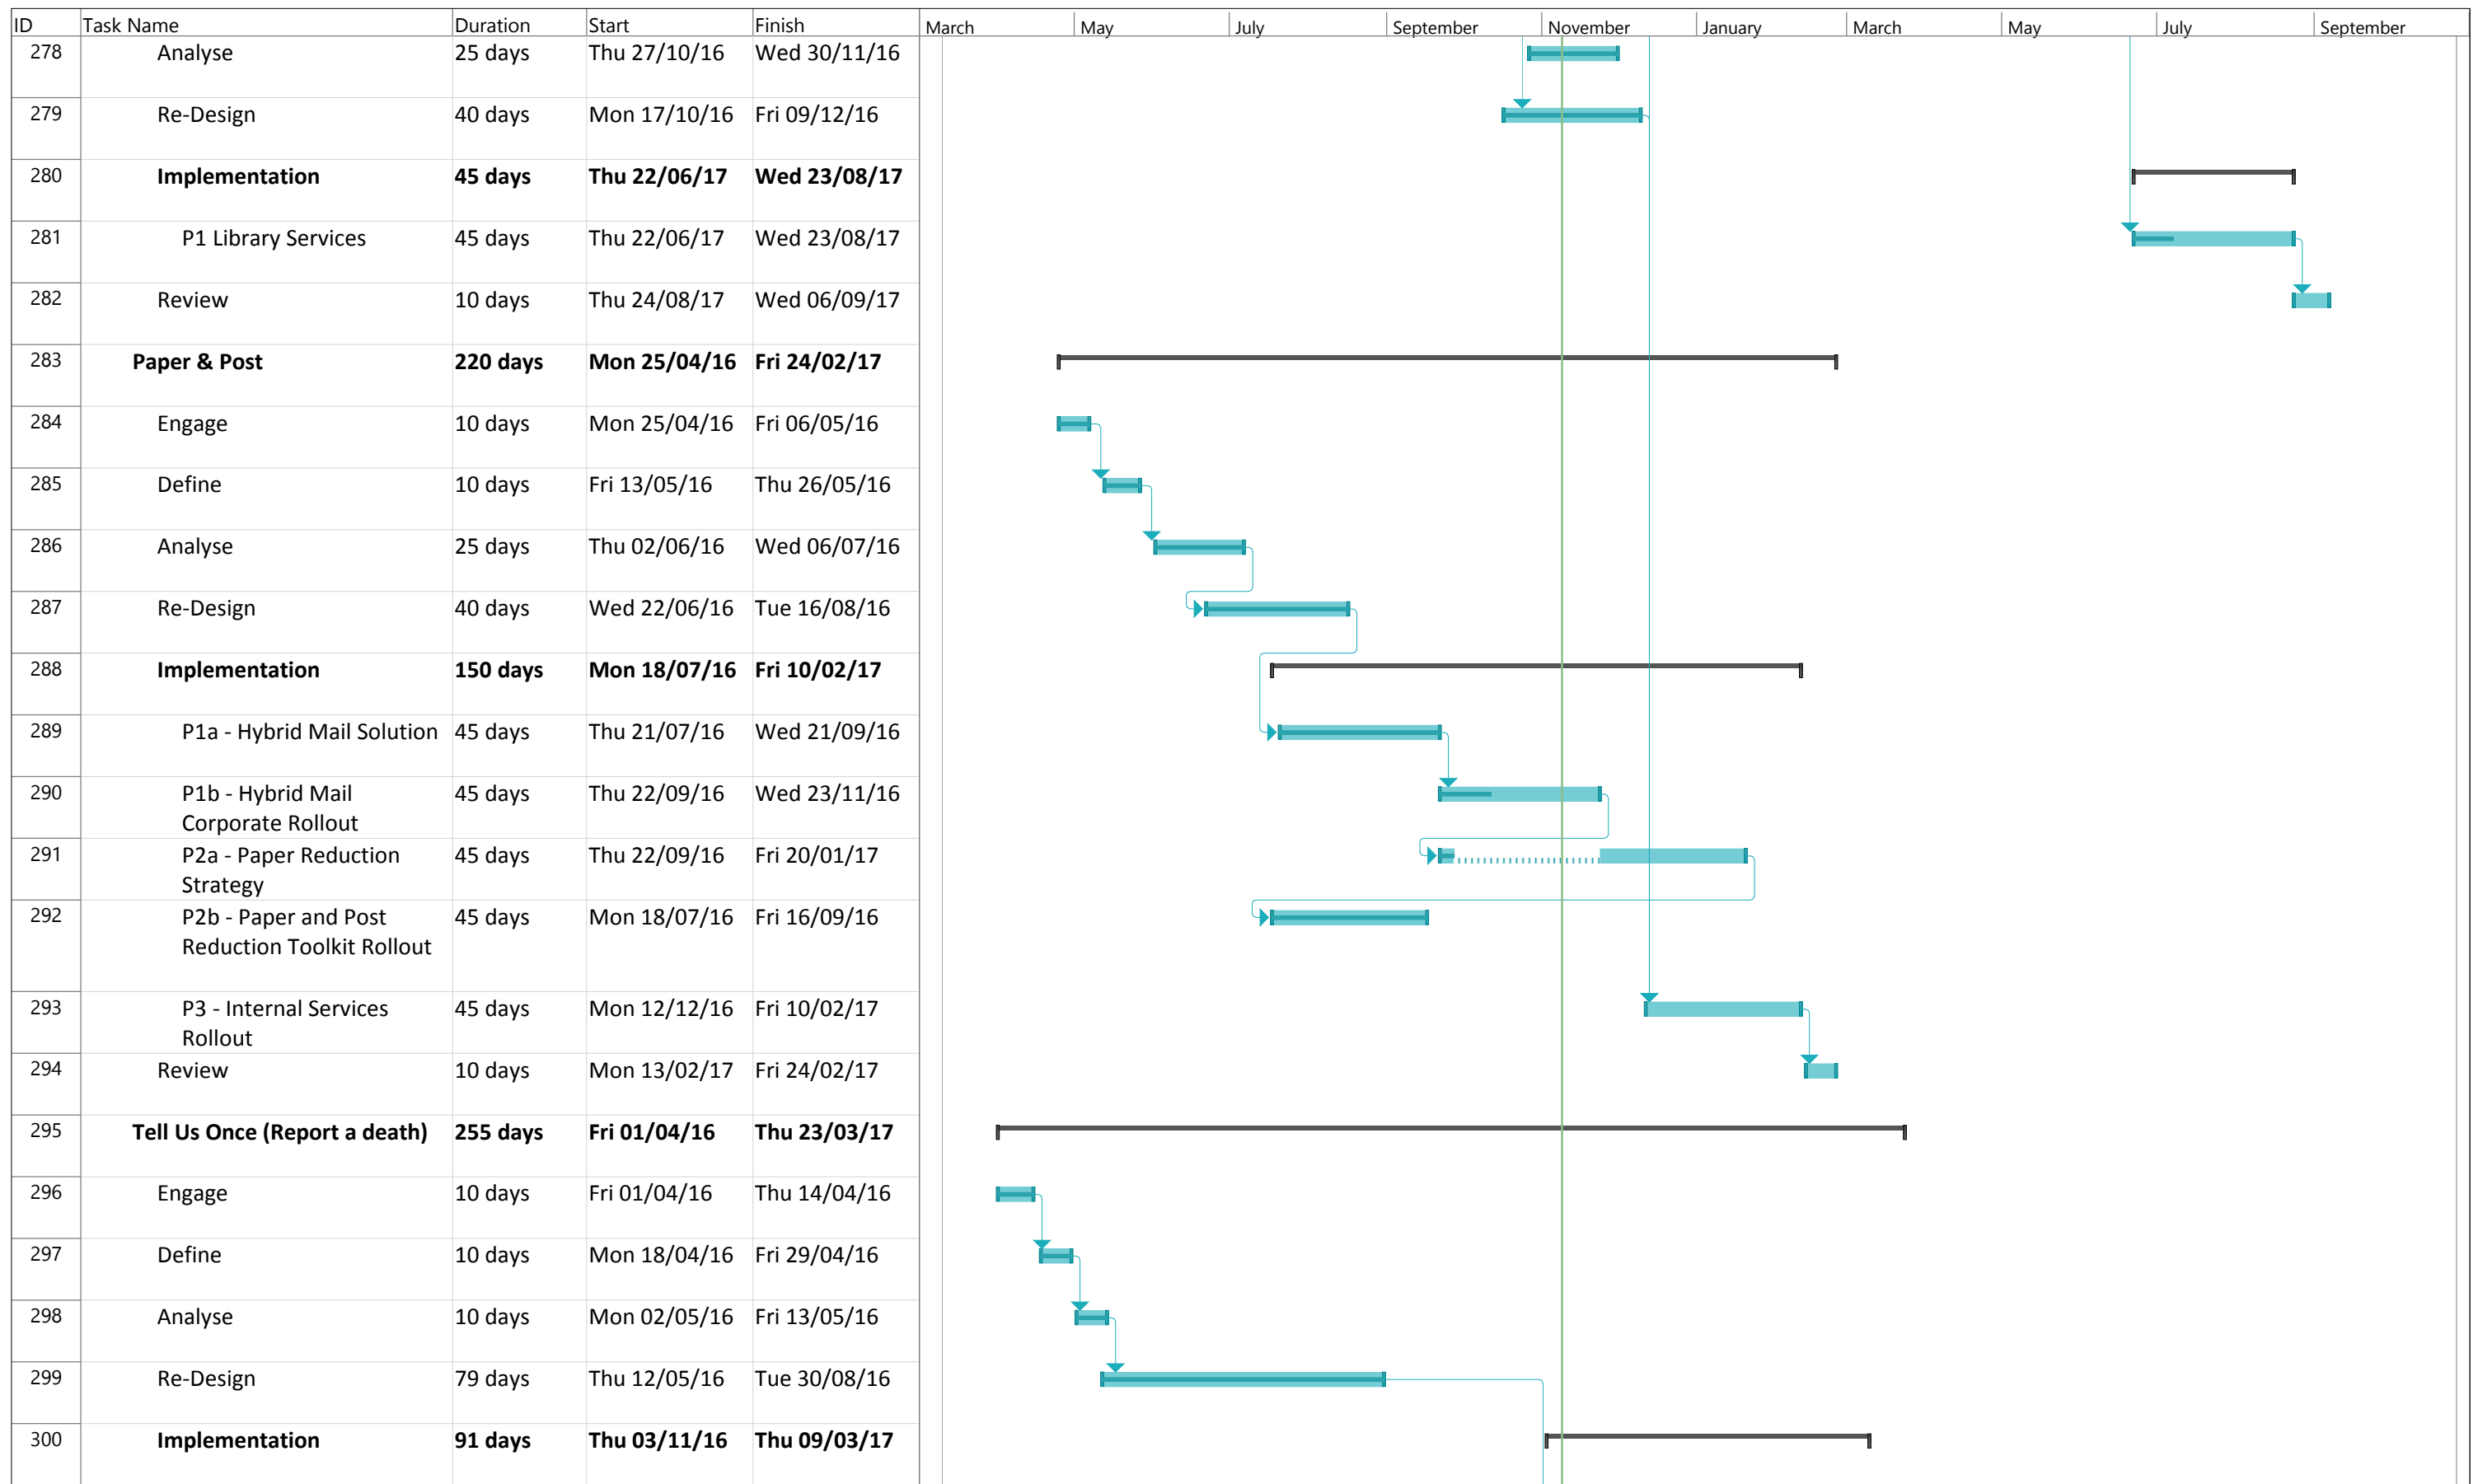

Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

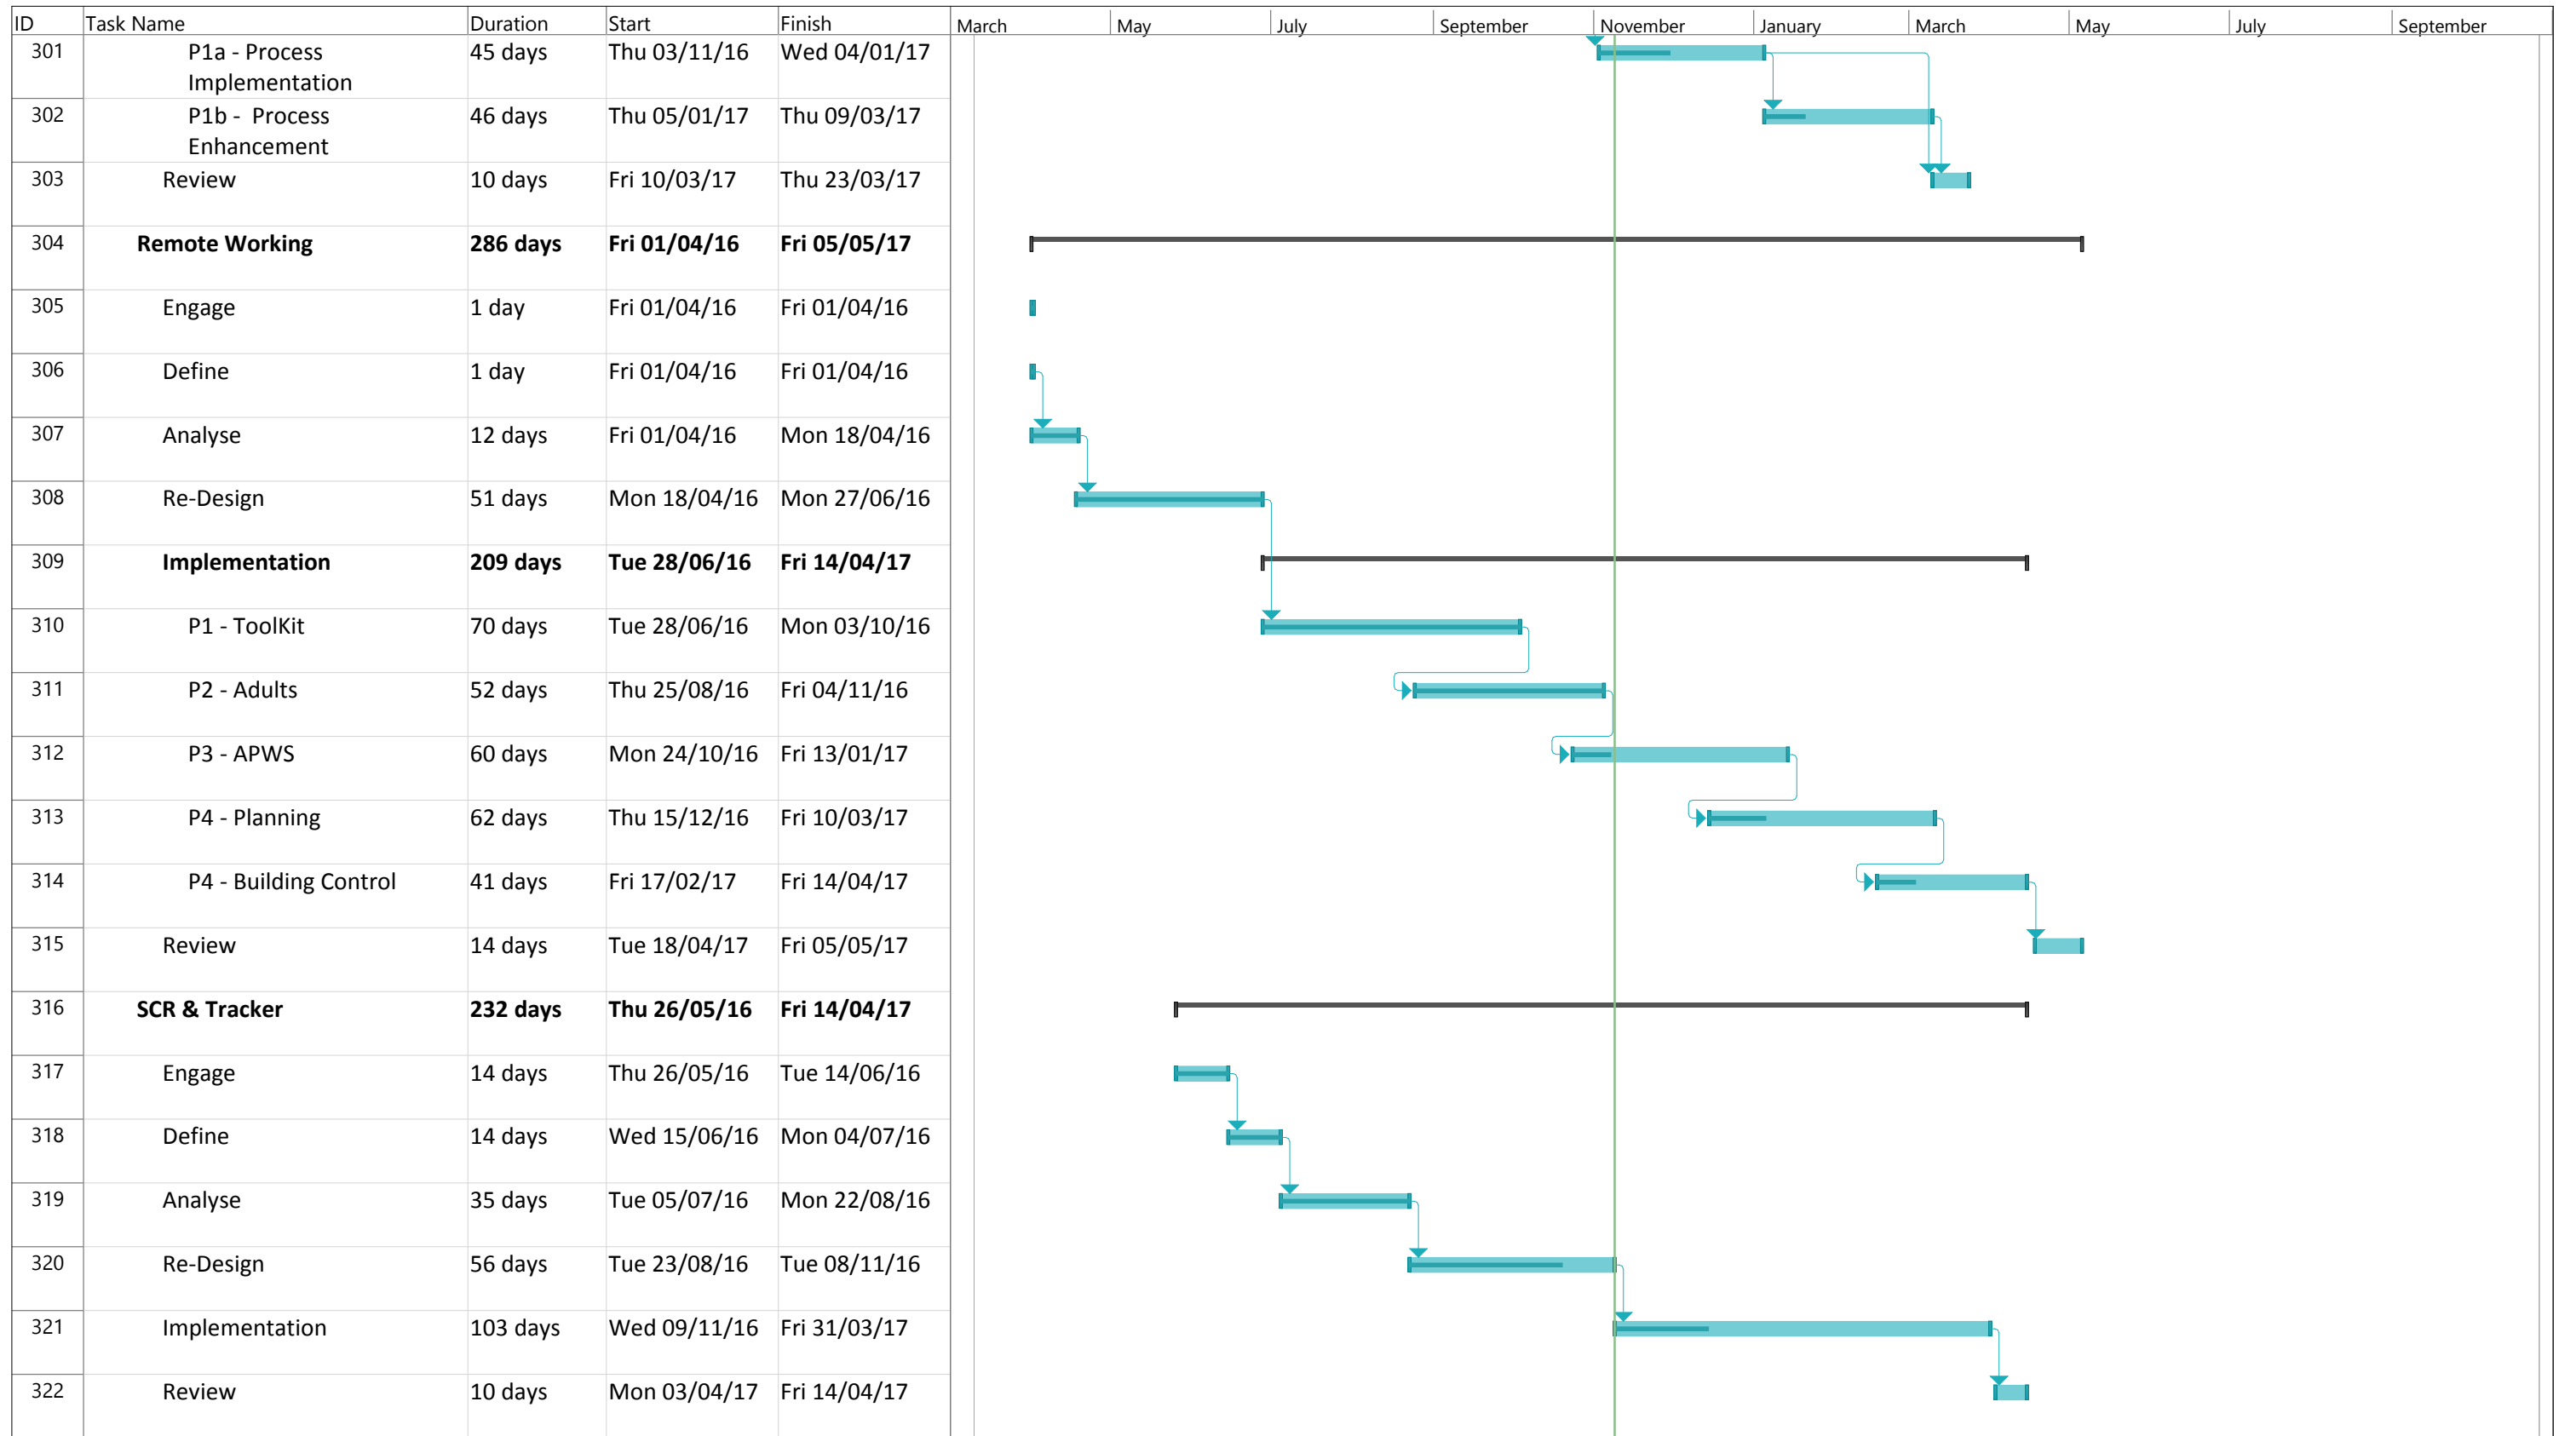

Project: Programme Plan - Sprin Date: Wed 09/11/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
